

Zamracka




Report On 2023

**CONSTITUENCY PROJECTS IN
ZAMFARA STATE**

Supported by:

MacArthur
Foundation

SUMMARY OF THE TRACKING EXERCISE



23

**TOTAL NUMBER
OF PROJECTS**

INTRODUCTION

Constituency projects tracking in Zamfara state is one of the activities of the Arewa Research & Development Project (ARDP): as one of the MacArthur Foundation's supported programs of the On Nigeria 2.0 Project. The strategic objectives are focused on reducing corruption through assisting community-based programs and efforts that would strengthen and systemize culture of accountability, transparency and popular participation in the conduct of public affairs. One of the key objectives of this activity is to determine the degree of involvement of the respective communities in the origin of the implementation of the constituency projects and their resourcefulness to societal needs. The activity is also expected to institutionalize or scale up citizens' participation in the incubation process of the constituency projects as well as to galvanize community-based drive in the monitoring and tracking of the projects. The activity is anchored by ZamTracka, which is a collaborative partner in Zamfara state.

ARDP is a research-based non-governmental, non-partisan, non-ethnic and non-religious organization dedicated to the study and examination of major contemporary challenges facing Northern Nigeria and its people, and to provide the needed framework for the strategic thinking and practical program of action needed to address those challenges. Its mission is to nurture the economic and social transformation of the region through undertaking projects that seek to bring together all northern social groups; pooling together the human and material resources in a manner that brings about strategic alliance and synergy with governmental and non-governmental organization working for the progress and well-being of the people in the region.

ZamTracka is a civil society organization based in Gusau, Zamfara state which seeks to champion the cause of civic advocacy with a view to entrenching social accountability in the state. Its main activities have been to source and simplify relevant data on the Zamfara state's fiscal budgets and Zonal intervention projects, and to use same to sensitize the public on the critical public information. The objective is to assist the citizens to follow up on the budgetary capital expenditures and other public projects in their respective communities. This is envisaged to create vanguards of active citizens that demand and ensure effective and efficient service delivery by governments and their agents, as well as stimulate and sustain the demand for open government in Zamfara state

Zonal intervention projects (popularly known as constituency projects) are public projects nominated by federal lawmakers to extend the dividends of democratic government to their various constituencies to spur development at the grassroots level of the country. The projects, by practice are recommended by the executive during the budgeting process. Constitutionally, the national assembly has the oversight obligation on government projects. Given the fact that these projects are nominated by lawmakers, they are morally and even more officially responsible to provide their people with the updates on every project domiciled in their constituency. This is because community member cannot easily access MDAs as they access their elected representatives. Noting that no lawmaker has direct control over the implementation of the projects aside from oversight function, legislators occupy a better position to monitor and proactively ensure the execution of every project by reaching out to the agencies in charge.

In 2022, the total sum of N1.52bn was allocated for constituency projects in Zamfara, the bulk of which are training/empowerment and projects. By way of example, for successive fiscal years, a project titled “Film grants” was nominated as one of the ZIPs in Zamfara state. The state is not known as a hub for film production or distribution to warrant preponderance of such a project in the state.

Capital projects typically involve physical infrastructure development, like building roads or schools, while training/empowerment projects focus on enhancing skills and capacities within a community. In Zamfara State, capital projects contribute to structural improvements, while training/empowerment projects aim to empower individuals and foster sustainable development through skill-building and education. Both play crucial roles in community development, addressing different aspects of growth and well-being. But the crux of the matter in Zamfara State is that the training/empowerment projects are hardly conceived and delivered in the manner to achieve the desired outcomes..

GUSAU/TSAFE FEDERAL CONSTITUENCY

Hon. Kabiru Amadu



01

Projects
nominated

01

Executed

0%

Empowerment
Projects

00

Unexecuted

100%

Capital Projects

Construction of all-in-one solar streetlights to boost agricultural activities in Gusau/Tsafe Federal Constituency.

The implementation of this project began on the 21st of December, 2023 and spanned across January, 2024. A total of the three different locations: Unguwan Yarima in Gusau, Wanzamai and the vicinity of General Hospital Tsafe were the beneficiaries of this project.

Field assessors however, were able to identify critical issues with the implementation of this project. The title of the project infers that the project seeks to boost agric and allied activities in the constituency but taking into cognizance the beneficiary locations, the impact is defeated. For example, Unguwan Yarima is the lawmaker's area of residence which is in an urban settlement with no inclination to agricultural activities. The remaining locations also do not support the project title as well.

Also, a total of just fifty-two (52) solar streetlights were installed overall with Unguwan Yarima, the lawmakers's area of residence receiving the highest number of installations, thirty (30) in all. The remaining two locations all in Tsafe shared the remaining Twenty-two (22). Taking another cursory look into the budgeted amount for this project, one could easily see that it is not commensurate with the expenditure and provides no value for money..

Conclusively, the end product of the project is mainly for aesthetics and visibility and not in any way boosting agricultural outcomes of the constituency. Thus, the impact of this project as it related to the title is significantly defeated. Furthermore, it is not known whether there is a post-project monitoring and maintenance system to conduce routine maintenance and repairs on faulty streetlights.



Gusau/Tsafe Federal Constituency

N121m

Executed



BUNGUDU/MARU FEDERAL CONSTITUENCY

Hon. AbdulMalik Zubairu



04

**Projects
nominated**

02

Executed

100%

**Empowerment
Projects**

02

Unexecuted

0%

Capital Projects

Supply of chairs and Desks to some primary schools in Maru/Bungude Federal Constituency.

This lawmaker unseated the incumbent in the last general elections in early 2023 and thus, he inherited this project from his predecessor. Regardless, this project was effectively implemented.

A fabricated steel work that combined a desktop and seat to form a single unit was utilized instead of separate units of chairs and desks. A total of 10 primary schools within the constituency received 50 pieces each.

Field assessors confirmed from the few beneficiary schools they were able to visit that the chronic shortage of seats has been greatly reduced by the intervention and some of the kids who were accustomed to either being cramped into the few available seats or sitting on the bare floor can now boast of a more comfortable space. This project will in no small measure increase the standard of the learning environment and thereby, improving the quality of teaching and learning.



Maru/Bungudu Federal Constituency

N21m

Executed



Supply of Sewing machines to women in Maru/Bungudu Federal Constituency.



Maru/Bungudu Federal Constituency

N25m

Executed

This project targeted members of the tailoring trade through their umbrella association in both local governments of the constituency. It was implemented on the 14th of January, 2024 in Bungudu Local Government and a total of Eighty-four (84) tailors majority of which were women, were given a brand new sewing machine each.

The most important point of note in the implementation process of this project is the fact that due diligence was done in terms of beneficiary selection as the right group of people were targeted. This infers that the beneficiaries will most likely retain and utilize the product to further improve on the productivity of their trade.

Thus, there is a clear prospect for impact. The fact that there is an umbrella body from which the beneficiaries were sought makes it easier for any sort of post-project monitoring and evaluation to be effectively conducted on beneficiaries.



Agribusiness capacity building and starter pack for women and youth in Maru/Bungudu Federal Constituency

The field assessors went round the constituency for proof of execution of this project but all responses were negative as constituents could not establish a case for its execution.



Maru/Bungudu Federal Constituency

N50m

Unexecuted



Supply of grains in Maru/Bungudu Federal Constituency

The field assessors went round the constituency for proof of execution of this project but all responses were negative as constituents could not establish a case for its execution.



Maru/Bungudu Federal Constituency

N25m

Unexecuted



BAKURA/MARADUN FEDERAL CONSTITUENCY

Hon. Muhammad Ahmed



03

**Projects
Nominated**

02

Executed

75%

**Empowerment
Projects**

01

Unexecuted

25%

Capital Projects

Training for rural women on modern renewable energy device for food processing and preservation in Bakura/Maradun Federal Constituency.



Bakura/Maradun
Federal Constituency

N40m

Executed



This lawmaker unseated the incumbent in the last general elections in early 2023 and thus, he inherited this project from his predecessor. Regardless, this project was executed however, the execution was flawed. The project was executed on the 19th of March in the premises of The college of agricultural sciences, Bakura Local Government. A total of 50 beneficiaries were trained and each received a token of N20,000 and a certificate of participation.

It is important to note that there is a disparity between the nominated project and the one implemented. All the beneficiaries were males with no single female and the focus of the training was specifically a basic tutorial on how solar technology works and not on using renewable energy for food processing and preservation. Also, the training lasted for just one day which is in stark contrast to the six (6) days captured on the project banner. All these factors support the fact that the project initially nominated was abandoned and replaced with a different one.

Also, taking into note the nominated amount for the implementation of the project and the shabby nature it was executed, it can be summarized as not having any value for money which makes any effort at evaluation and impact assessment to be futile.



Supply and installation of solar streetlights in Bakura/Maradun Federal Constituency.



Bakura/Maradun
Federal Constituency

N51m

Executed

The implementation of this project commenced on the 21st, December, 2023. The actual number of streetlights could not be verified as at the time of filing this report.

However, field assessors were able to sample some locations that have benefitted from this project in order to conduct needs assessment so as to understand whether or not the intervention addresses any pressing need or challenge.

The outcome was positive because most of the locations had visibility challenges mostly at night and with the deteriorating security situation, it helps to illuminate the areas and also boost liveliness of the areas. Some of the locations included mosques, Islamic schools, open markets and deep rural enclaves.

It is not known whether there is a post-project monitoring and maintenance system to conduct routine maintenance and repairs on faulty streetlights.



Construction of 2 solarpowered boreholes in Bakura/Maradun Federal Constituency.

The field assessors went round the constituency for proof of execution of this project but all responses were negative as constituents could not establish a case for its execution.



Bakura/Maradun
Federal Constituency

N30m

Unexecuted

ZAMFARA WEST SENATORIAL DISTRICT

Sen. AbdulAziz Yari



01

**Projects
Nominated**

01

Executed

0%

**Empowerment
Projects**

00

Unexecuted

100%

Capital Projects

Supply and installation of solar streetlights to enhance agric outputs in Zamfara West Senatorial District.



Zamfara West
Senatorial District

N214m

Executed

This lawmaker unseated the incumbent in the last general elections in early 2023 and thus, he inherited this project from his predecessor. The implementation of this project started in December, 2023 through January, 2024. The actual number of streetlights could not be verified as at the time of filing this report.

However, field assessors were able to sample some locations that have benefitted from this project namely: Titin 'yar Yelwa, Titin 'Yar Hudu, 'Yan Kifi, Karfi Area, 'Yar Zamau and Titin Stadium all within the zone in order to conduct needs assessment so as to understand whether or not the intervention helps in enhancing agricultural outcomes of the senatorial zone as captured in the project's title. The outcome was negative as most of the areas were semi urban and it is hard to link them to any agro-allied activity. Thus, it is fair to say the project is mainly for aesthetics and visibility at night and not in any way boosting agricultural outcomes of the zone.

It is not known whether there is a post-project monitoring and maintenance system to conduct routine maintenance and repairs on faulty streetlights.



GUMMI/BUKKUYUM FEDERAL CONSTITUENCY

Hon. Sulaiman Abubakar



03

**Projects
Nominated**

02

Executed

75%

**Empowerment
Projects**

01

Unexecuted

25%

Capital Projects

Completion of primary healthcare center at Gamji in Gummi/Bukkuyum Federal Constituency.

This project was initiated in November, 2020 but was abandoned for more than three (3) years until now. It is a 31 beds primary healthcare center located in Gamji area of Illela ward, Gummi Local Government. Thus, this intervention sought to complete the structure and ready it for public use.

Field assessors were able to track the implementation of this project and were fortunate enough to meet workers on site. All structural works were completed and only the painting of the structure remained. What is not known is when the facility will be fully furnished and open to public.

Taking a cursory look at the demography of the wards and its environs, this facility when completed and commissioned will be the only active major healthcare facility in the entire region with the potential to tender to patients from far away regions. Thus, the impact of this project is clearly visible.

However, most of interventions like this fail to attain the lofty heights envisioned during their inception simply because there is no robust involvement of community leadership in the running and maintenance of the facilities. Thus, it is hoped that this will be different so that the community takes ownership of the intervention and ensures its sustainability.



Gummi/Bukkuyum
Federal Constituency

N31m

Executed



Supply of 18 seater Bus in Gummi/Bukkuyum Federal Constituency.



Gummi/Bukkuyum
Federal Constituency

N50m

Executed !

The supply of this 18 seater bus was officially declared on the 16th of March, 2024 at an event which took place at the premises of the lawmaker's constituency office in Gummi Local Government. No less than 10 other vehicles were declared on the same day, albeit they were shared to some designated loyalists of the lawmaker.

The 18 seater bus had a sticker on it indicating that it is a utility vehicle for student affairs within the constituency, however, the need to procure this vehicle for same purpose cannot be established. There are also grave concerns on who takes custody of the vehicle, what the need scope of usage is and who becomes responsible for its recurrent needs.

The concerns our founded on the outcomes we have seen from similar projects we tracked over the last couple of years where the vehicle after launch, automatically becomes an addition to the lawmaker's fleet of cars and does not in anyway benefit the constituency. Recall also that last year, the lawmaker nominated a similar project to procure a constituency vehicle which was not executed at all.

Also, N50m was allotted for this project but after thorough examination of the vehicle, it is implausible for it to cost that amount. The market value of a brand new Toyota 18 seater bus is within the range of N27m-N29m and the one procured and supplied is a used one. So there is no value for money expended on the project.



Development of value chain addition and large ruminants through processing for market access and economic empowerment in Gummi/Bukkuyum Federal Constituency

The field assessors went round the constituency for proof of execution of this project but all responses were negative as constituents could not establish a case for its execution.



Gummi/Bukkuyum
Federal Constituency

N40m

Unexecuted

KAURA/BIRNIN MAGAJI FEDERAL CONSTITUENCY

Hon. Aminu Sani Jaji



02

**Projects
Nominated**

02
Executed

100%
**Empowerment
Projects**

00
Unexecuted

0%
Capital Projects

Skill acquisition for youth and women in Kaura/Birnin Magaji Federal Constituency.

N25m

Executed !

This lawmaker unseated the incumbent in the last general elections in early 2023 and thus, he inherited this project from his predecessor. Regardless, this project was implemented in two (2) days, from the 17th to the 19th of July, 2023 at the Federal Polytechnic, Kaura Namoda.

A total of One Hundred (100) beneficiaries enlisted from the Twenty-One wards of the constituency were trained for two days essentially on cosmetology which included liquid soap making and Vaseline. At the end of the training, each of the beneficiaries received a certificate of attendance and a token of N15,000 as a startup capital with which to start a small scale business.

Based on trends we have seen over the years from the implementation of this kind of project, it is difficult to establish impact because the right beneficiaries are not the ones trained and there is no post-project monitoring and evaluation in order to ascertain its impact on the beneficiaries and the constituency as a whole. Thus, most trainees become dormant post-project because even the token given as startup capital is spent on other necessities rather than the skill learnt.

It is thus, pertinent that interventions like this are anchored on the targeting the right pool of trainees and a post-project evaluation plan so that impact and sustainability are brought to fore.



Supply of agricultural inputs in Kaura/Birnin Magaji Federal Constituency.

N50m

Executed 

This lawmaker unseated the incumbent in the last general elections in early 2023 and thus, he inherited this project from his predecessor. Regardless, this project was implemented on the 17th of July, 2023 at the Federal Polytechnic, Kaura Namoda. It was implemented on the same day the previous project was commenced.

The total number of beneficiaries could not be established as at the time of compiling this report. However, reports indicate that the beneficiaries were real time farmers from the Twenty-One (21) wards of the constituency.

It is worthy of note that the constituency is an agrarian one which makes agricultural interventions such as this very necessary. However, this project only saw each beneficiary get one single sack of fertilizer which could be grossly inadequate.



SHINKAFI/ZURMI FEDERAL CONSTITUENCY

Hon. Bello Hassan



03

**Projects
Nominated**

03

Executed

75%

**Empowerment
Projects**

00

Unexecuted

25%

Capital Projects

Renovation and construction of drainage in Shinkafi town in Shikafi/Zurmi Federal Constituency

N100m

Executed

The commencement of implementation of this project was on the 12th of November, 2023. Several wards in Shinkafi Local government with communities that are water-logged and prone to erosion were effectively targeted for this intervention.

Field assessors were able to go round some of the wards to assess the quality of the construction as well as its impact on the communities. The quality of work is satisfactory as steel reinforced concrete technique was used throughout the project. However, the only concern raised is the fact that the drainage is a bit shallow and may overflow during heavy downpours.

Also, they are not covered and may act as a breeding ground for mosquitoes that causes malaria if they are not properly drained and maintained. Apart from one location in Katuru ward that the project was not fully completed, all have been fully completed.

Thus, the impact of this intervention on the constituency is tangible and in this period of climate change where rain patterns are unpredictable, this intervention will go a long way in addressing the problem the constituency is facing in this regard.



Supply of gas cylinders in Shinkafi/Zurmi Federal Constituency

N21m

Executed

This project is not a supply of gas cylinders to the constituency. It is a robust empowerment project targeting petty traders. It was executed on the 17th of June, 2023. A total of 180 beneficiaries who either tea and bread sellers, beans cake sellers or soya beans cake sellers were sourced from the Twenty-One (21) wards of the constituency: Shinkafi North, Shinkafi South and Zurmi ward produced Twelve (12) beneficiaries each while the remaining 18 wards produced eight (8) beneficiaries each.

Among the items distributed on that day were cartons of Indomie quick noodle, Gallons of Groundnut oil, Sack of beans, large frying pans and 3kg gas cylinders. This intervention seeks to support small scale trading and the mode of execution is different from the trends we have seen over the years.

The right pool of beneficiaries were targeted and instead of giving petty cash as startup capital that have no guarantee to be injected into the trade, they were all empowered by items and they need today to start business or upscale today and not tomorrow. This gives a high prospect for impact and sustainability. However, it is not established that a post-project monitoring and evaluation framework is in place to assess directly, impact and challenges.



Educational empowerment to the students of Shikafi/Zurmi Federal Constituency

N50m

Executed



This is an intervention necessitated by the hike in tuition fees for public Universities nationwide. The constituency is among the least educated and developed in the state and thus, it is pertinent to support those who have managed to seek tertiary education.

The exact framework for the implementation of this project is not clear as field assessors could not establish the amount each student-beneficiary got in order to see whether the amount is homogenous or not. Also, the criteria for selection of beneficiaries is not clear as well as the total number of beneficiaries in the support scheme.

Field assessors were able to sight a list from a batch of beneficiaries from Usmanu Danfodio University in Sokoto consisting of all their corresponding details. However, it is not known which other university or institution is captured under the scheme.




NAME	ADDRESS	PHONE	EMAIL
...



NAME	ADDRESS	PHONE	EMAIL
...



NAME	ADDRESS	PHONE	EMAIL
...



NAME	ADDRESS	PHONE	EMAIL
...

ZAMFARA NORTH SENATORIAL ZONE

Sen. Sahabi Ya'u



02

**Projects
Nominated**

00

Executed

100%

**Empowerment
Projects**

02

Unexecuted

0%

Capital Projects

Empowerment for women and youths of Zamfara North Senatorial District.

The field assessors went round the constituency for proof of execution of this project but all responses were negative as constituents could not establish a case for its execution.



Zamfara North
Senatorial District

N100m

Unexecuted

Agro-business supplies for small scale farmers in Zamfara North Senatorial District.

The field assessors went round the constituency for proof of execution of this project but all responses were negative as constituents could not establish a case for its execution.



Zamfara Northe
Senatorial District

N100m

Unexecuted

ZAMFARA CENTRAL SENATORIAL ZONE

Sen. Ikira Aliyu Bilbis



01

**Projects
Nominated**

00
Executed

100%
**Empowerment
Projects**

01
Unexecuted

0%
Capital Projects

NHIS vital health contribution to social health insurance scheme in Zamfara Central Senatorial District.

The field assessors went round the constituency for proof of execution of this project but all responses were negative as constituents could not establish a case for its execution.



Zamfara Central
Senatorial District

N214m

Unexecuted

ANKA/MAFARA FEDERAL CONSTITUENCY

Hon. Muhd Isa Anka



03

**Projects
Nominated**

02

Executed

75%

**Empowerment
Projects**

01

Unexecuted

25%

Capital Projects

Training for rural women on modern renewable energy devise for food processing and preservation in Anka/Mafara Federal Constituency

N41m

Executed

This lawmaker unseated the incumbent in the last general elections in early 2023 and thus, he inherited this project from his predecessor. Regardless, this project was implemented on the 9th of March, 2024 at Karma Hotel, Gusau.

A total of 50 women were transported to Gusau, the state capital for the training. This decision was largely due to the volatile security situation in the constituency and its environ. The training was basically a lecture session where they were taught on the renewable energy and the various forms it can be used to aid food processing (cooking) and its preservation.

At the end of the session, each of the beneficiary was given a pellet-fueled stove and a token of N20,000. Field assessors could not establish was criteria was used to select the beneficiaries as most appeared to be not into a trade that this intervention could support. Thus, the impact of this intervention is difficult to establish.

In terms of value for money, the total amount given to beneficiaries as start-up capital amounts to N1million. Even though it is difficult to establish the actual cost of the stoves that were distributed, the basic nature in which the project was implemented is not commensurate with the total amount allotted for the project. Thus, this project does not satisfy the value for money criterion.



Provision of skill acquisition equipments in Anka/Mafara Federal Constituency.

N30m

Executed

This project was implemented on the 9th of March, 2024 at Karma Hotel, Gusau. A total of 50 beneficiaries were transported to Gusau, the state capital for the training and this decision to implement the project outside the constituency was largely due to the volatile security situation in the constituency and its environ.

The training was basically a lecture session and a hands-on training on renewable energy with specific focus on how to harness solar energy for domestic and commercial use. During the training, they were shown the basics of how to couple a solar energy system effectively. It is this basic introduction that the beneficiaries are expected to hinge their foray into entrepreneurship on.

At the end of the session which lasted for a day, each of the beneficiary was given a token of N20,000 as a startup grant to enable them startup a venture. Field assessors could not establish was criteria was used to select the beneficiaries and whether or not any post-project monitoring and evaluation framework is in place to assess project impact.

In terms of value for money, the total amount given to beneficiaries as start-up capital amounts to N1million. Also, the basic nature in which the project was implemented is not commensurate with the total amount allotted for the project. Thus, this project does not satisfy the value for money criterion.



Supply and installation of integrated solar streetlights in Anka/Mafara Federal Constituency.

The field assessors went round the constituency for proof of execution of this project but all responses were negative as constituents could not establish a case for its execution.



Anka/Mafara
Federal Constituency

N50m

Unexecuted


METHODOLOGY

This looks at whether Citizens' Engagement avenues such as town hall meeting were used to engage citizens in the nomination process.



Any Civic engagement strategy utilized takes 1 point. its absence is an automatic 0.

This reviews the level of execution of all project Nominated by the respective law-makers.

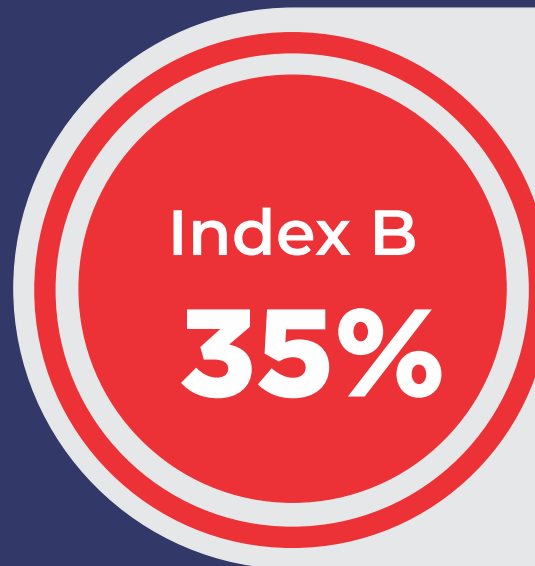

$$\frac{\text{Executed Projects}}{\text{Total Number of Projects}}$$

Index C Looks at the project nomination and draws distinction between capital project and not so impactful Empowerment/Project



$$\frac{\text{Capital Projects Nominated}}{\text{Total Number of Projects}}$$

Lawmaker Performance on **Index A**

Index A looks whether Citizens' Engagement avenues such as town hall meeting were used to engage citizens in the nomination and execution process.

Lawmaker	Index A Rating
Sen. Muhammad Hassan	0
Sen. Sahabi Ya'u	0
Sen. Lawali Hassan	0
Hon. Kabiru Amadu	0
Hon. Shehu Ahmed	0
Hon. Umar Dangaladima	0
Hon. Ahmad Muhammad	0
Hon. Kabiru Yahaya	0
Hon. Sulaiman Abubakar Gummi	0
Hon. Bello Hassan Shinkafi	0

Lawmaker Performance on **Index B**

Index B assesses level of project completion. Lawmakers that rank higher on this index have a higher project completion rate.

Lawmaker	Index B Rating
Sen. Muhammad Hassan	1
Sen. Sahabi Ya'u	1
Hon. Shehu Ahmed	1
Hon. Umar Dangaladima	1
Hon. Ahmad Muhammad	1
Hon. Bello Hassan Shinkafi	1
Hon. Kabiru Yahaya	0.75
Hon. Kabiru Amadu	0.66
Hon. Sulaiman Abubakar Gummi	0.66
Sen. Lawali Hassan	0

Lawmaker Performance on **Index C**

Representatives with a higher ranking on Index C have prioritized capital projects in their nominations. While in contrast, those with lower ranking nominated projects that are not legacy based and whose real impact cannot be fully determined

Lawmaker	Index C Rating
Sen. Sahabi Ya'u	1
Hon. Shehu Ahmed	0.33
Sen. Muhammad Hassan	0
Hon. Umar Dangaladima	0
Hon. Ahmad Muhammad	0
Hon. Bello Hassan Shinkafi	0
Hon. Kabiru Yahaya	0
Hon. Sulaiman Abubakar Gummi	0
Hon. Kabiru Amadu	0
Sen. Lawali Hassan	0

2022 Zamfara Federal Lawmakers' Constituency Projects Performance index

Ranking	Lawmaker	Constituency	Commulative Index Score
1st	Sen. Sahabi Ya'u	Zamfara North Zone	2
2nd	Hon. Shehu Ahmed	Bungudu/Maru	1.33
3rd	Sen. Muhammad Hassan	Zamfara Central Zone	1
3rd	Hon. Umar Dangaladima	Kaura/Birnin Magaji	1
3rd	Hon. Ahmad Muhammad	Bakura/Maradun	1
3rd	Hon. Bello Hassan Shinkafi	Shinkafi/Zurmi	1
7th	Hon. Kabiru Yahaya	Anka/Mafara	0.75
8th	Hon. Kabiru Amadu	Gusau/Tsafe	0.66
8th	Hon. Sulaiman Abubakar	Gummi/Bukkuyum	0.66
10th	Sen. Lawali Hassan	Zamfara West	0

STATISTICAL BREAKDOWN



Total Amount Allotted

N1.52bn


29

Soft Projects

03

Hard Projects

PERCENTAGE OF PROJECTS' COMPLETION

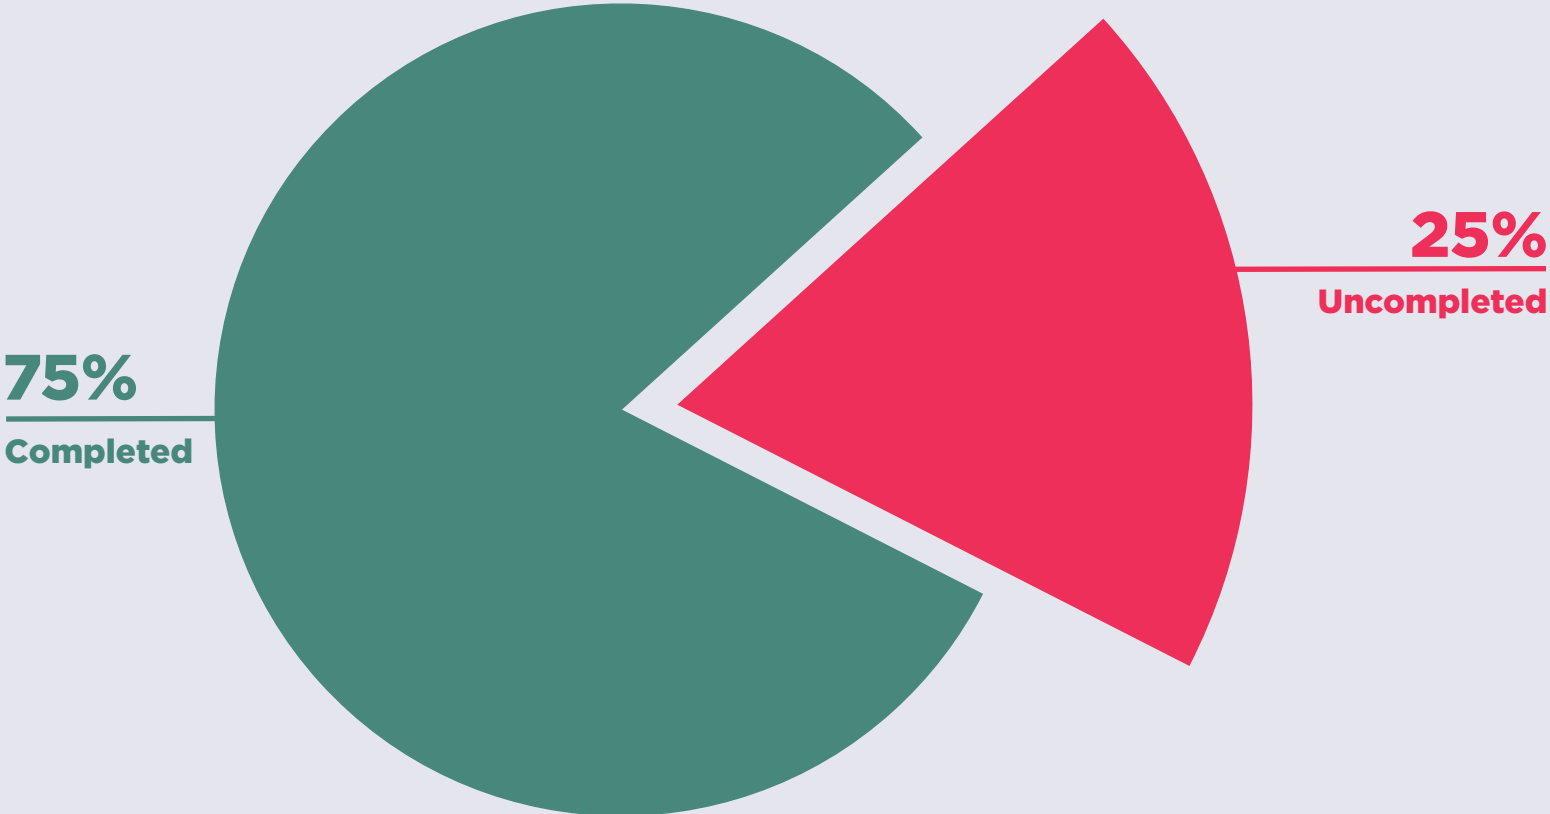



Follow up and track implementation of public projects within your vicinity



Upload pictures, add comments, send feedback to institutions



Announce and share with your friends, family and thousand across the state



Continue to engage.

No. 40, Sadiqu Sadiq Road,
Tudun Wada, Gusau, Zamfara State.

 [f/t](#) [@ZamTracka](#)

 ZamTracka@gmail.com
